

N°	Modèle	Nom de la tâche	Durée	Début	Fin	Prédécesseurs	Remarques	02 Sep 24							09 Sep 24							16 S
								D	L	M	M	J	V	S	D	L	M	M	J	V	S	
0		Projet aménagement MANTES U	635 jours?	Dim 01/09/24 09:00	Jeu 18/02/27 18:00																	
1		1 STRATEGIE GENERALE	338 jours?	Dim 01/09/24 09:00	Jeu 18/12/25 09:00																	
20		2 PROCEDURES REGLEMENTAIRES	1 jour?	Lun 02/09/24 09:00	Lun 02/09/24 18:00																	
55		3 ETUDES	1 jour?	Lun 02/09/24 09:00	Lun 02/09/24 18:00																	
64		4 COMMERCIALISATION	1 jour?	Lun 02/09/24 09:00	Lun 02/09/24 18:00																	
68		5 TRAVAUX	635 jours?	Lun 02/09/24 09:00	Jeu 18/02/27 18:00																	
69		5.1 ESPACES PUBLICS	573 jours?	Mer 27/11/24 09:00	Jeu 18/02/27 18:00																	
70		5.1.1 LOT M1	573 jours?	Mer 27/11/24 09:00	Jeu 18/02/27 18:00																	
71		5.1.1.1 ETUDES MOE	288 jours?	Mer 27/11/24 09:00	Mer 07/01/26 18:00																	
72		5.1.1.1.1 Notification AVP	0 jour	Mer 27/11/24 09:00	Mer 27/11/24 09:00																	
73		5.1.1.1.2 Envoi dossier AVP à GPSEO	0 jour	Mar 28/01/25 09:00	Mar 28/01/25 09:00																	
74		5.1.1.1.3 Remarques AVP de GPSEO	0 jour	Lun 17/03/25 09:00	Lun 17/03/25 09:00																	
75		5.1.1.1.4 Obtention permission de voirie de GPSEO	0 jour	Lun 07/04/25 09:00	Lun 07/04/25 09:00																	
76		5.1.1.1.5 Présentation PRO à GPSEO	0 jour	Ven 20/06/25 09:00	Ven 20/06/25 09:00																	
77		5.1.1.1.6 Notification PRO A AOR	0 jour	Jeu 11/09/25 09:00	Jeu 11/09/25 09:00																	
78		5.1.1.1.7 Remarques PRO de GPSEO	0 jour	Lun 15/09/25 09:00	Lun 15/09/25 09:00																	
79		5.1.1.1.8 Rendu DCE	0 jour?	Ven 10/10/25 09:00	Ven 10/10/25 09:00																	
80		5.1.1.1.9 Lancement consultation	5 semaines	Ven 10/10/25 09:00	Ven 14/11/25 18:00	79	voir T.C delais juridiques															
81		5.1.1.1.10 Remise offre et analyse	4 semaines	Lun 17/11/25 09:00	Ven 12/12/25 18:00	80																
82		5.1.1.1.11 CAO	1 jour	Lun 15/12/25 09:00	Lun 15/12/25 18:00	81																
83		5.1.1.1.12 Notification marché de travaux	3 semaines	Mar 16/12/25 09:00	Mer 07/01/26 18:00	82																
84		5.1.1.2 TRAVAUX	315 jours?	Mer 17/09/25 09:00	Jeu 10/12/26 18:00																	
85		5.1.1.2.1 Travaux provisoires	98 jours?	Mar 15/07/25 09:00	Ven 28/11/25 18:00																	
86		5.1.1.2.1.1 Travaux ENEDIS	54 jours	Mar 15/07/25 09:00	Ven 26/09/25 18:00																	
87		5.1.1.2.1.2 Bon de commande entreprise Bailleuse	0 jour	Mer 17/09/25 09:00	Mer 17/09/25 09:00																	
88		5.1.1.2.1.3 Agrément sous traitants	0 jour	Sam 27/09/25 09:00	Sam 27/09/25 09:00	87																
89		5.1.1.2.1.4 Obtention arrêté municipal	0 jour	Lun 29/09/25 09:00	Lun 29/09/25 09:00	87																
90		5.1.1.2.1.5 Réalisation du génie civil orange	13 jours	Mer 01/10/25 09:00	Ven 17/10/25 18:00	87																
91		5.1.1.2.1.6 Réalisation raccordement SEFO	1 jour?	Mer 17/09/25 09:00	Mer 17/09/25 18:00		attente arrêté ville															
92		5.1.1.2.1.7 Réalisation raccordement EU EP	42 jours?	Mer 01/10/25 09:00	Ven 28/11/25 18:00																	
93		5.1.1.2.1.8 Démolition dalles béton	0 jour?	Ven 24/10/25 09:00	Ven 24/10/25 09:00																	
94		5.1.1.2.1.9 Date de libération base vie	0 jour?	Mer 17/09/25 09:00	Mer 17/09/25 09:00																	
95		5.1.1.2.1.10 Réalisation des accès VL et piétons phase 1 AD	1 mois	Mar 07/10/25 09:00	Lun 03/11/25 18:00	87																
96		5.1.1.2.1.11 Pose BAV	0 jour	Ven 28/11/25 09:00	Ven 28/11/25 09:00																	
97		5.1.1.2.1.12 Livraison agronergy	0 jour	Jeu 16/10/25 09:00	Jeu 16/10/25 09:00																	
98		5.1.1.2.2 Travaux définitifs phase 1 ADIM	120 jours	Jeu 08/01/26 09:00	Ven 26/06/26 18:00	83																
99		5.1.1.2.2.1 Période de préparation	1 mois	Jeu 08/01/26 09:00	Mer 04/02/26 18:00	83																
100		5.1.1.2.2.2 Travaux	5 mois	Jeu 05/02/26 09:00	Ven 26/06/26 18:00	99																
101		5.1.1.2.3 Travaux définitifs phase 2 LEGENDRE	6 mois	Mar 01/09/26 09:00	Jeu 18/02/27 18:00																	
102		5.1.1.2.3.1 période de préparation	1 mois	Mar 01/09/26 09:00	Lun 28/09/26 18:00																	
103		5.1.1.2.3.2 Travaux	5 mois	Mar 29/09/26 09:00	Jeu 18/02/27 18:00	102																
104		5.2 Halle Sulzer	1 jour?	Lun 02/09/24 09:00	Lun 02/09/24 18:00																	
105		5.3 Dépollution	1 jour?	Lun 02/09/24 09:00	Lun 02/09/24 18:00																	
106		5.4 OPC-OPCU	1 jour?	Lun 02/09/24 09:00	Lun 02/09/24 18:00																	
107		5.5 Démolition	1 jour?	Lun 02/09/24 09:00	Lun 02/09/24 18:00																	
108		6 FONCIER	1 jour?	Lun 02/09/24 09:00	Lun 02/09/24 18:00																	
114		7 COMMUNICATION	1 jour?	Lun 02/09/24 09:00	Lun 02/09/24 18:00																	




[illegible]

[illegible]





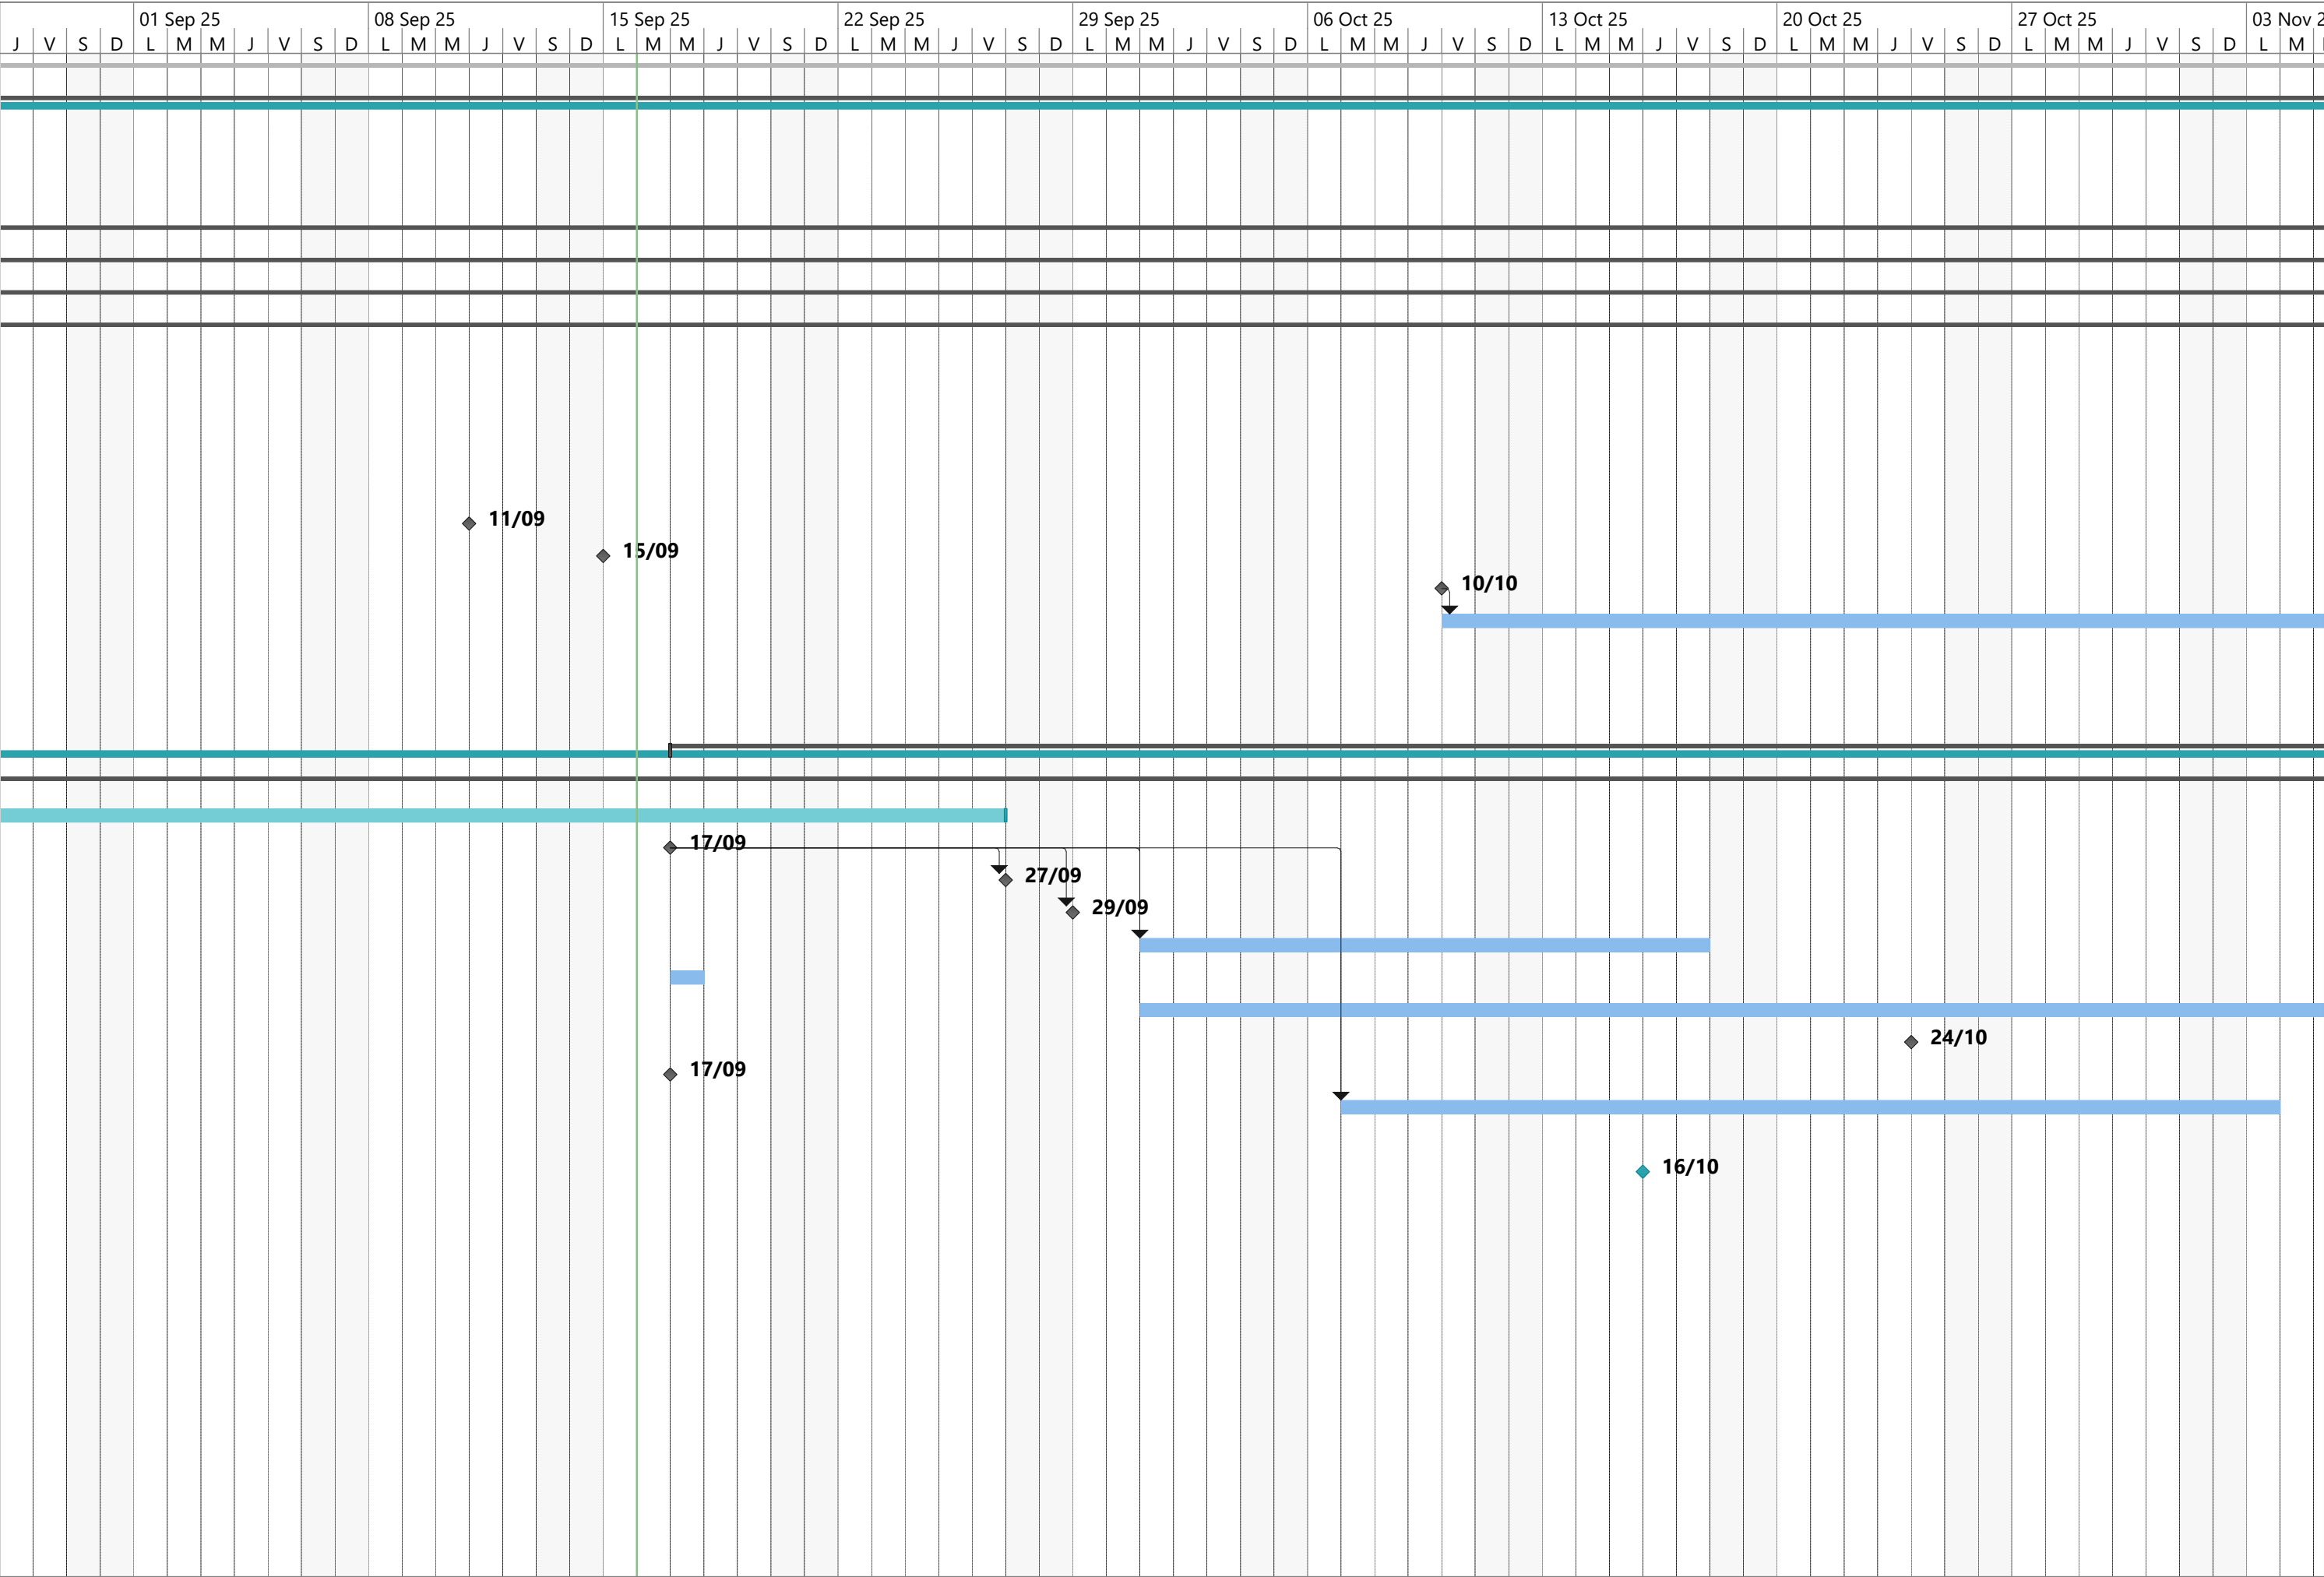







[illegible]





[illegible]

[illegible]
