


Diagramme de Gantt

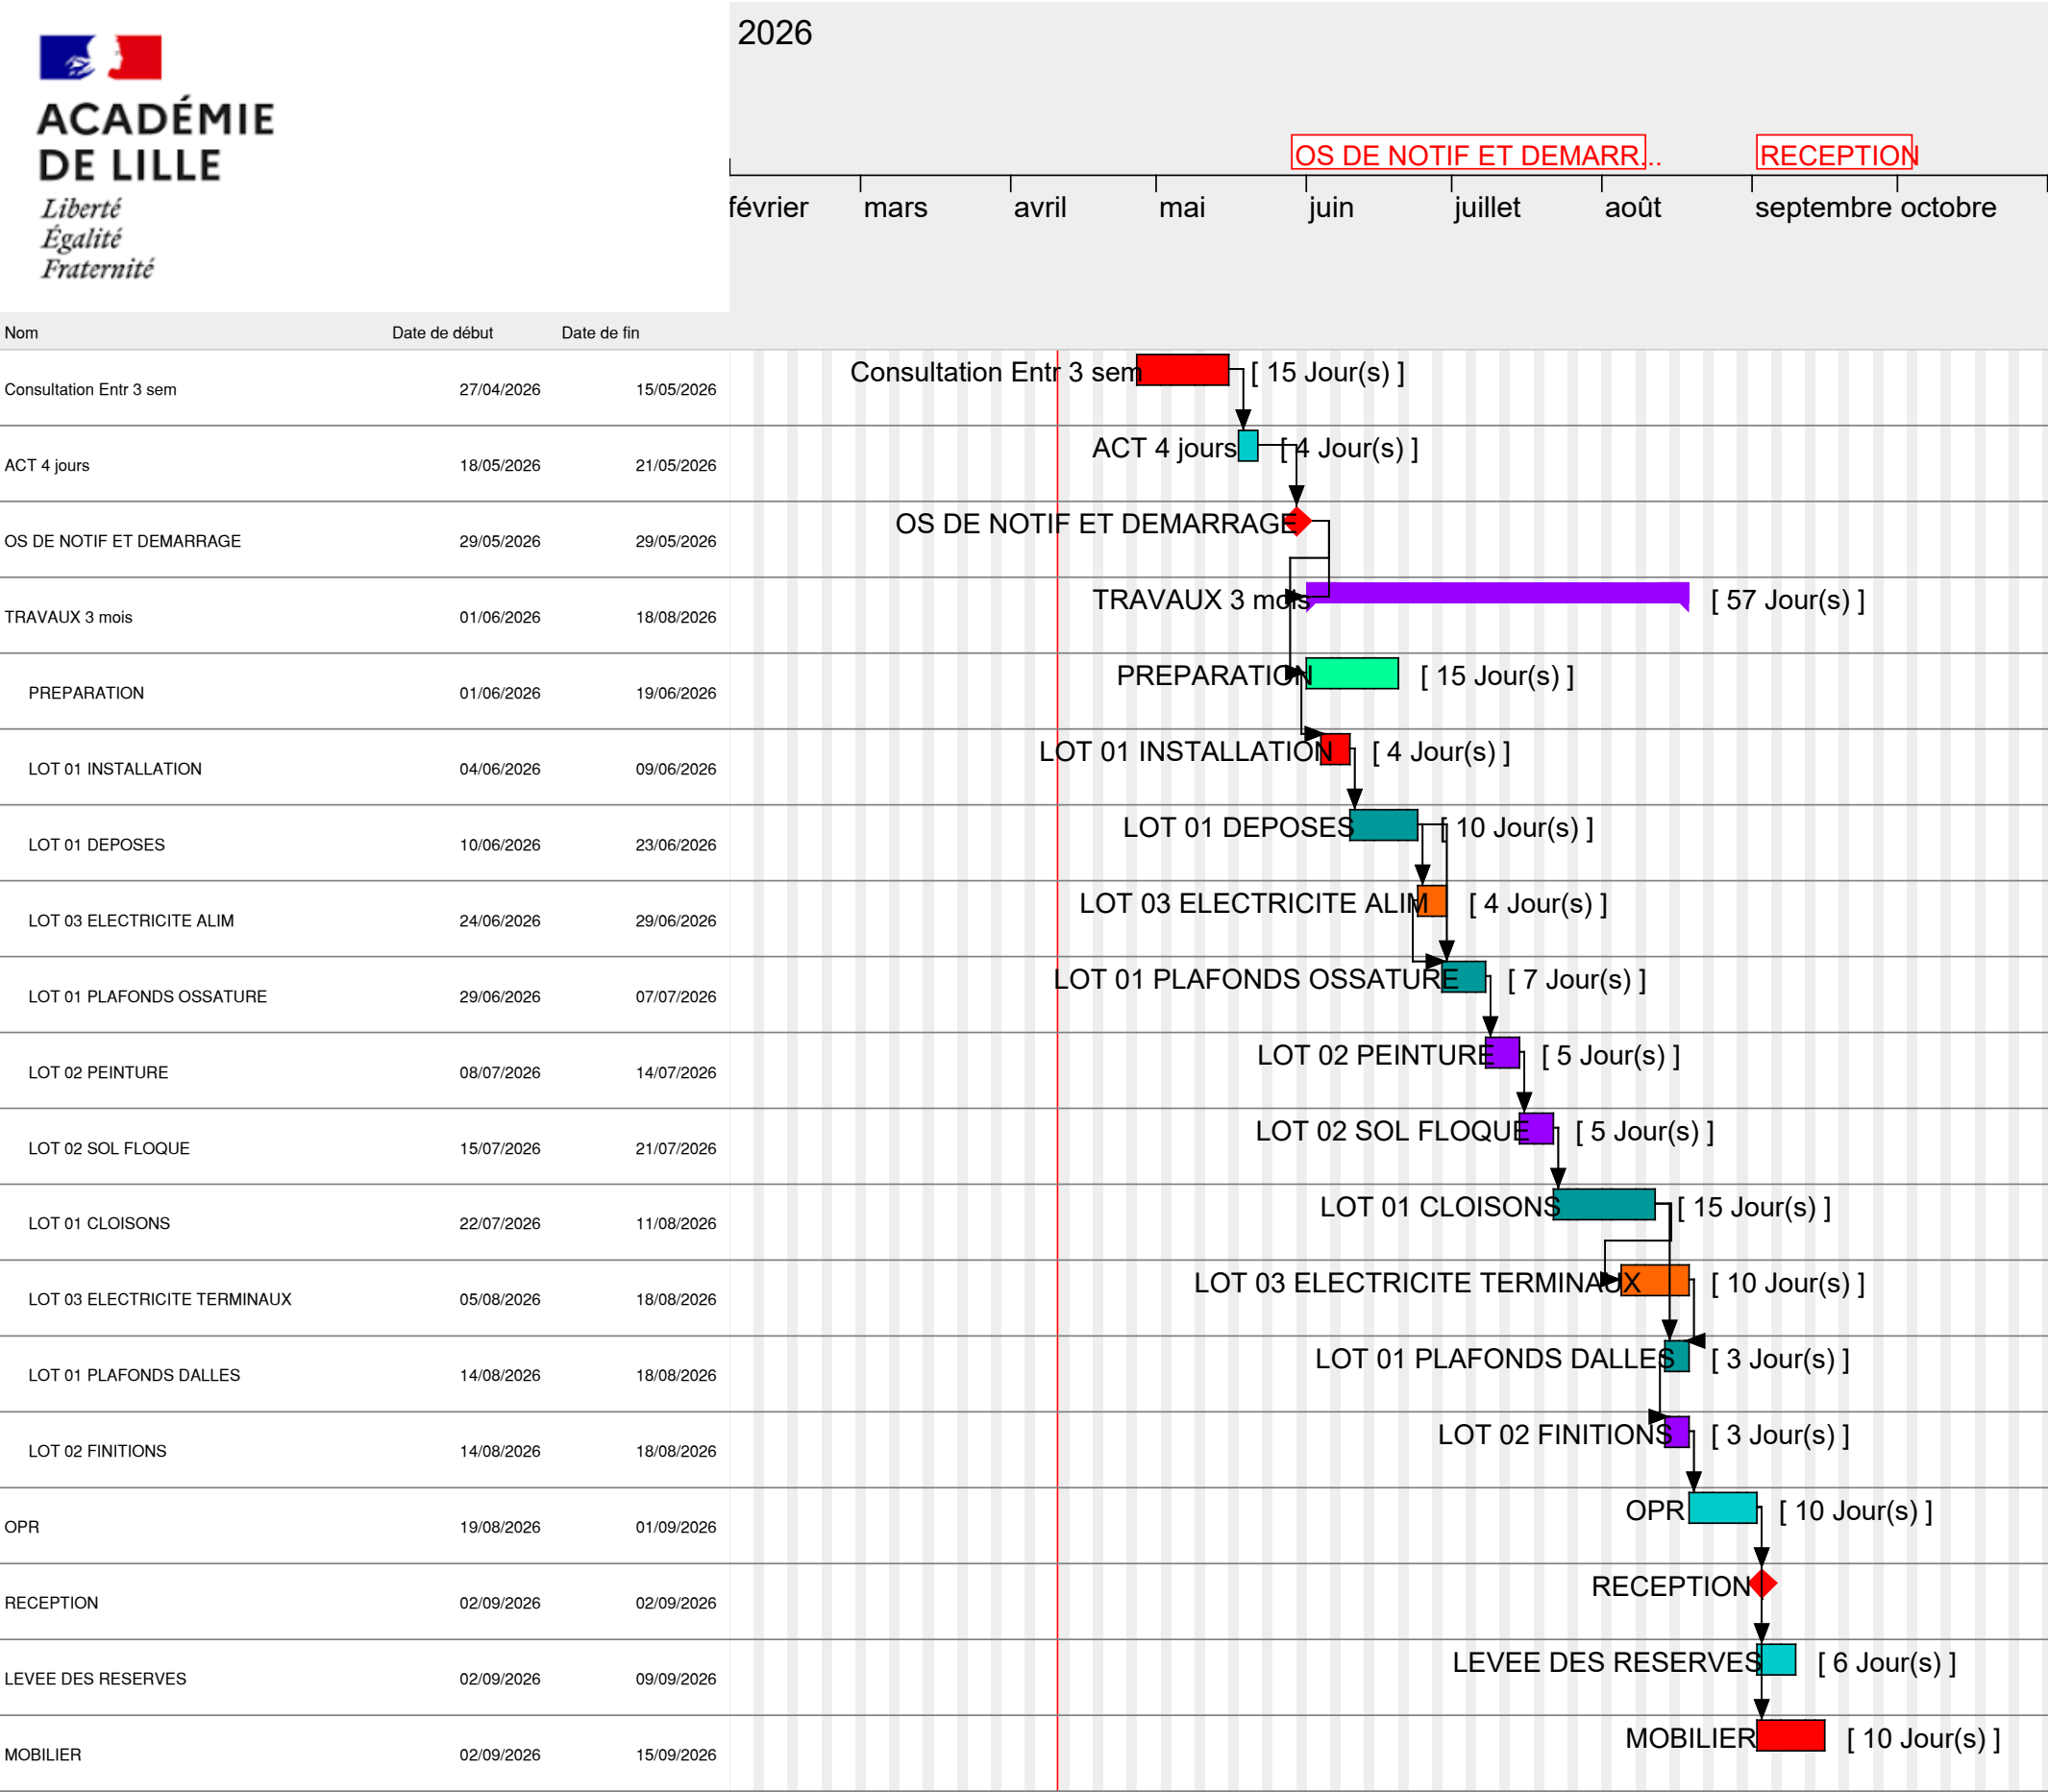

Consultation Entr 3 sem

[15 Jour(s)]

ACT 4 jours

[4 Jour(s)]

OS DE NOTIF ET DEMARRAGE

TRAVAUX 3 mois

[57 Jour(s)]

PREPARATION

[15 Jour(s)]

LOT 01 INSTALLATION

[4 Jour(s)]

LOT 01 DEPOSES

[10 Jour(s)]

LOT 03 ELECTRICITE ALIM

[4 Jour(s)]

LOT 01 PLAFONDS OSSATURE

[7 Jour(s)]

LOT 02 PEINTURE

[5 Jour(s)]

LOT 02 SOL FLOQUE

[5 Jour(s)]

LOT 01 CLOISONS

[15 Jour(s)]

LOT 03 ELECTRICITE TERMINAUX

[10 Jour(s)]

LOT 01 PLAFONDS DALLES

[3 Jour(s)]

LOT 02 FINITIONS

[3 Jour(s)]

OPR

[10 Jour(s)]

RECEPTION

LEVEE DES RESERVES

[6 Jour(s)]

MOBILIER

[10 Jour(s)]
